

From progress to a working MVP.

ICT Tools Assets Management and Support System
with an AI chatbot companion.

FOCUS FOR THE NEXT 7 DAYS: CONNECT. STABILIZE. SIMPLIFY. DOCUMENT.

7

DAYS TO DELIVER

Target:

one reliable,
demonstrable web MVP —
not the entire final
platform.

MURI / INTERNAL DELIVERY
PLAN

One system. Three outcomes.

01

Support

Staff raise IT tickets and receive clear resolution progress.

02

Asset control

IT personnel manage vouchers, assets, disposal records, and documents.

03

Assistance

An Ollama-powered chatbot helps users find answers and understand procedures.

TARGET MVP JOURNEY

→ Login

→ Dashboard

→ Raise ticket /
manage asset

→ Track status

→ Resolve & document

The foundation is already visible.

COMPLETED WORK

Identity	• Done	Name and color changes
Direction	• Done	Vision and mission
Experience	• Done	Dashboard visibility
Interfaces	• Done	Admin and User dashboards
Database	• Started	MySQL → PostgreSQL correction
AI	• Started	Ollama chatbot foundation

The gap is not the idea.

The gap is turning the visible foundation into one connected, testable workflow.

Not every missing feature has the same urgency.

P0

Critical blockers

MUST BE SOLVED FIRST

Backend down.

MySQL → PostgreSQL migration incomplete.

Backend logic not linked to dashboards.

Login path needs demo method.

P1

Simplify for MVP

MAKE SMALL AND USABLE

Make **Vouchers** and **Assets** functional.

Give Disposal, Documents, and Settings MVP states.

Measure Ollama response time with a small FAQ test.

Write concise setup and user docs.

P2

Defer beyond week

DO NOT SPLIT THE TEAM

Dedicated native **mobile app**.

Full institutional email / SSO integration.

Advanced chatbot optimization and coverage.

Complex permissions, reporting, and production hardening.

DELIVERY LOGIC

Stabilize the backend first, then connect one complete ticket-and-asset journey. Everything else should support that demo or move to the next phase.

Build the MVP, not the whole platform.

The fastest route to a credible result is to make one core workflow reliable, then represent the remaining breadth honestly.

P0 / MUST WORK BY DAY 7

The connected core

- Backend + PostgreSQL
- Ticket workflow
- Access + dashboards
- AI companion

MVP STATE / KEEP LIGHT

Useful breadth

- Logistics
- Other logistics pages
- Institutional email
- Mobile readiness

DEFER / NEXT PHASE


Do not overload the week

- Native mobile app
- Advanced AI tuning
- Enterprise hardening

DECISION: If a feature does not help the Day 7 demo journey, it is not a P0 feature this week.

Seven days. One connected workflow.

01	Stabilize environment	Backend runs; dependencies and variables recorded.
02	Finish migration	PostgreSQL schema, seed data, and essential CRUD paths work.
03	Connect backend logic	Ticket creation, listing, status updates, and errors work end-to-end.
04	Minimum logistics	Vouchers and Assets work; other pages have clear MVP states.
05	Access and AI	Simple login works; chatbot baseline is measured on curated questions.
06	Test and document	Critical journeys pass; setup guide and limitations are written.
07	Demo hardening	Blocking defects fixed; demo data, rehearsal, and next backlog ready.

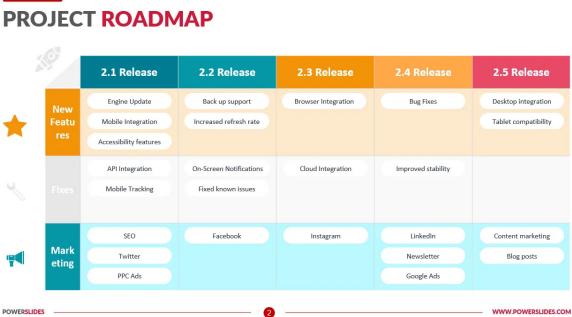

Order matters.

Recover the backend and database first. Add features only after the core path can be tested from login to resolution.


DEFINITION OF DONE

On Day 7, the audience can see a working MVP –not seven disconnected workstreams.

Protect the critical path.


Relative allocation for this seven-day sprint – a planning model, not a measure of completed hours.

WORKSTREAM	PRIORITY	RELATIVE EFFORT
Backend recovery + PostgreSQL	P0	30%
Ticket workflow integration	P0	20%
Minimum logistics dashboard	P0	20%
Login + access control	P1	10%
Ollama baseline + tuning	P1	10%
Testing + documentation	P0	10%

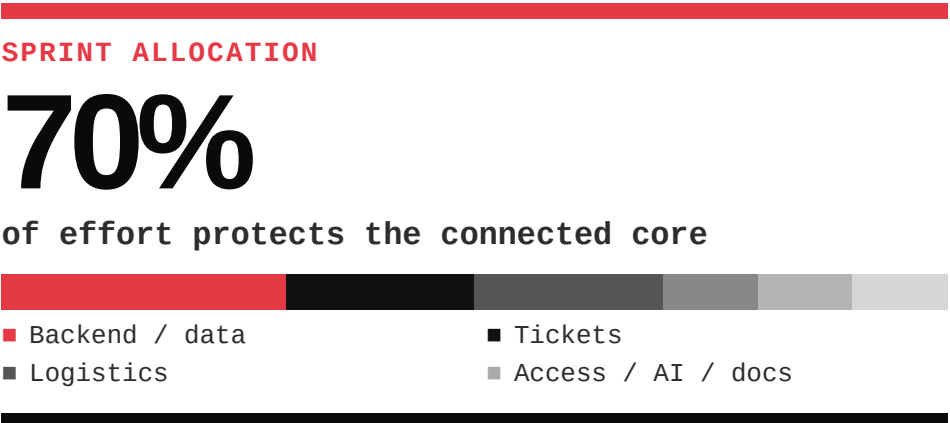

A full mobile app, enterprise login, complete logistics, backend integration, AI optimization, and documentation are too much for one week if all are treated as production-ready.

The MVP should reduce complexity, not reduce usefulness.

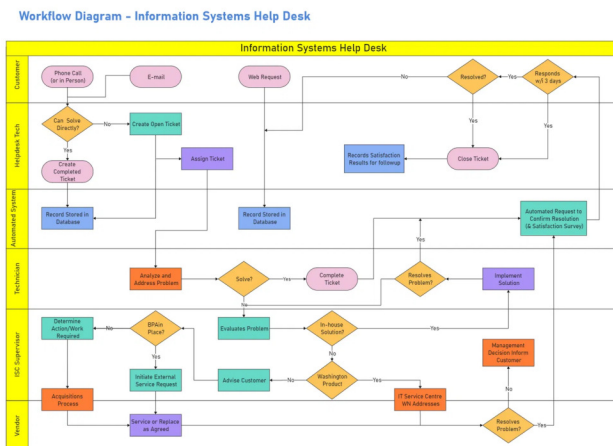

Use one visible path from request to resolution.
Additional branches become next-phase decisions
unless they block the core journey.

- | | | |
|----|------------------------|--|
| 01 | One active database | Use PostgreSQL as the single active source. Remove migration ambiguity before adding features. |
| 02 | One ticket lifecycle | Start with four statuses: New, In Progress, Resolved, Closed. |
| 03 | Two logistics entities | Make Assets and Vouchers functional; keep Disposal, Documents, and Settings simple. |
| 04 | One chatbot boundary | Use a curated FAQ and measure Ollama with a repeatable question set. |
| 05 | Responsive web first | Make the current web interface phone-friendly; build native mobile after the backend stabilizes. |

OPERATING PRINCIPLE Choose the smallest implementation that proves the workflow, then expand from a stable foundation.


Prove the journey, not the feature count.

The audience should see one staff request move through the system and come back as a documented resolution.

01	Staff logs in	User reaches the correct dashboard with a simple working access path.
02	Raises a ticket	Staff describes an ICT problem and submits the request.
03	Admin reviews	Admin opens the Admin Dashboard and sees the new ticket.
04	Status changes	Admin moves the ticket through New, In Progress, or Resolved.
05	Asset is checked	Admin opens Logistics and demonstrates a voucher or asset record.
06	AI assists	Staff asks a supported question and receives a bounded chatbot answer.

IT Support Help Desk Process for Fixing Technical Issues

This template covers about help desk process for IT technology support with user roles like customer, service admin, service agent with detailed process activities

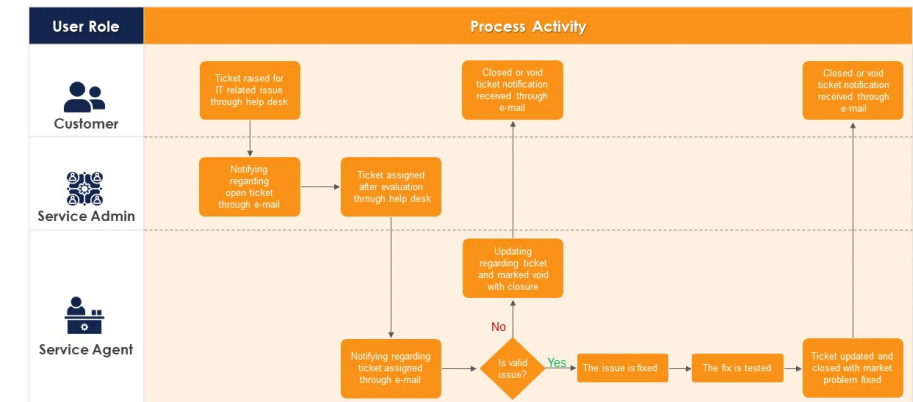

This slide is 100% editable. Adapt it to your needs and capture your audience's attention.

Keep the demo path linear: request → triage → status → asset context → answer.

SUCCESS CONDITION

Connected and understandable. The audience sees a working core that can be tested, demonstrated, and extended.

Protect the promise. Control the risk.

The best Day 7 outcome is a reliable core that can be demonstrated, tested, and extended—not a larger collection of unfinished features.

RISK	IMMEDIATE RESPONSE
Backend remains down	Assign one person to recovery only on Day 1.
Migration defects	Freeze schema changes after Day 2 and test the essential paths.
Email-provider access is missing	Use a temporary demo login and document the dependency.
Ollama is slow	Reduce knowledge scope, measure a baseline, and optimize obvious bottlenecks.
Scope expands during the week	Apply a strict P0 / P1 / defer rule to every new request.

DAY 7 TARGET

MVP
A responsive web system with one complete support-and-asset journey.

PostgreSQL-backed tickets, minimum Assets and Vouchers, bounded AI assistance, and concise documentation.

NEXT PHASE, NOT THIS WEEK

Dedicated mobile application
Institutional email / SSO

FINAL RECOMMENDATION

MURI is not starting from zero. Connect, stabilize, simplify, and document the core experience now; expand from a stable foundation next.
